CALIFORNIA REGIONAL WATER QUALITY CONTROL BOARD

CENTRAL VALLEY REGION
11020 SUN CENTER DR #200
RANCHO CORDOVA CA 95670-6114

2023 ANNUAL REPORT

PREPARED FOR:

MONSTER DAIRY

1048 LUNDY RD

NEWMAN CA 95360

NOTES:

PREPARED BY:

CARDOSO AG SERVICES

PO BOX 906
NEWMAN CA 95360

Annual Report - General Order No. R5-2007-0035
Reporting period 01/01/2023 to 12/31/2023.

DAIRY FACILITY INFORMATION

A. NAME OF DAIRY OR BUSINESS OPERATING THE DAIRY: Monster Dairy

Physical address of dairy:

Number and Street	City	County	Zip Code
1048 Lundy Rd	Newman	Stanislaus	95360

Street and nearest cross street (if no address):

Date facility was originally placed in operation: 01/01/1970

Regional Water Quality Control Board Basin Plan designation: San Joaquin River Basin

County Assessor Parcel Number(s) for dairy facility:

X049-X032-X003-XXXX

B. OPERATORS

Barcellos, Mike

Operator name: Barcellos, Mike

Telephone no.: Landline: ; Cellular: (209) 678-1792

Mailing Address Number and Street	City	State	Zip Code
1048 Lundy RD	Newman	CA	95360

This operator is responsible for paying permit fees.

C. OWNERS

Barcellos, Joe

Legal owner name: Barcellos, Joe

Telephone no.: Landline: (209) 595-2075; Cellular:

Mailing Address Number and Street	City	State	Zip Code
1054 Lundy RD	Newman	CA	95360

Annual Report - General Order No. R5-2007-0035
Reporting period 01/01/2023 to 12/31/2023.

AVAILABLE NUTRIENTS

A. HERD INFORMATION

	Milk Cows	Dry Cows	Bred Heifers (15-24 mo.)	Heifers (7-14 mo. to breeding)	Calves (4-6 mo.)	Calves (0-3 mo.)
Number open confinement	0	0	236	208	65	58
Number under roof	450	63	0	0	0	0
Maximum number	450	63	236	208	65	58
Average number	450	63	236	208	65	58
Avg live weight (lbs)	1,200	1,250	875	550		

Predominant milk cow breed: Jersey-Holstein Cross

Average milk production: 63 *pounds per cow per day*

B. MANURE GENERATED

Total manure excreted by the herd: 16,704.60 *tons per reporting period*

Total nitrogen from manure: 206,005.90 *lbs per reporting period*

After ammonia losses (30% loss applied): 144,204.13 *lbs per reporting period*

Total phosphorus from manure: 33,754.04 *lbs per reporting period*

Total potassium from manure: 84,109.60 *lbs per reporting period*

Total salt from manure: 226,369.35 *lbs per reporting period*

C. PROCESS WASTEWATER GENERATED

Process wastewater generated: 6,250,090 *gallons*

Total nitrogen generated: 36,742.02 *lbs*

Total phosphorus generated: 4,885.73 *lbs*

Total potassium generated: 56,734.04 *lbs*

Total salt generated: 268,308.04 *lbs*

	6,250,090	*gallons applied*
+	0	*gallons exported*
-	0	*gallons imported*
=	6,250,090	*gallons generated*

D. FRESH WATER SOURCES

Source Description	Type
Canal	Surface water
Domestic Well	Ground water

E. SUBSURFACE (TILE) DRAINAGE SOURCES

No subsurface (tile) drainage sources entered.

F. NUTRIENT IMPORTS

No dry manure nutrient imports entered.

No process wastewater nutrient imports entered.

No commercial or other nutrient imports entered.

G. NUTRIENT EXPORTS

Date	Material type	Quantity	Reporting basis	Moisture (%)	Density (lbs/cu ft)	N (mg/kg)	P (mg/kg)	K (mg/kg)	Salt (mg/kg)	TFS (%)
05/22/2023	Corral solids	3,666.00 *ton*	Dry-weight	73.5		21,200.00	4,800.00	28,900.00		0.00

No liquid nutrient exports entered.

Material type	Total N (lbs)	Total P (lbs)	Total K (lbs)	Total salt (lbs)
Dry manure	41,191.18	9,326.30	56,152.12	0.00
Process wastewater	0.00	0.00	0.00	0.00
Total exports for all materials	41,191.18	9,326.30	56,152.12	0.00

APPLICATION AREA

A. LIST OF LAND APPLICATION AREAS

Field name	Controlled acres	Cropable acres	Total harvests	Type of waste applied	Parcel number
1	41	41	2	process wastewater	X049-X032-X003-XXXX
2/3	29	29	2	process wastewater	X049-X032-X003-XXXX
Totals for areas that were used for application	70	70	4		
Totals for areas that were not used for application					
Land application area totals	70	70	4		

B. CROPS AND HARVESTS

1

Field name: 1

09/30/2022: Oats, silage-soft dough

Crop: Oats, silage-soft dough Acres planted: 41 Plant date: 09/30/2022

Harvest date	Yield	Reporting basis	Density (lbs/cu ft)	Moisture (%)	N (mg/kg)	P (mg/kg)	K (mg/kg)	Salt (mg/kg)	TFS (%)
05/01/2023	779.00 *ton*	Dry-weight		70.0	19,800.00	4,800.00	33,000.00		9.80

	Yield (tons/acre)	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Salt (lbs/acre)
Anticipated harvest content	16.00	160.00	25.60	132.80	0.00
Total actual harvest content	19.00	225.72	54.72	376.20	1,117.20

05/15/2023: Corn, silage

Crop: Corn, silage Acres planted: 41 Plant date: 05/15/2023

Harvest date	Yield	Reporting basis	Density (lbs/cu ft)	Moisture (%)	N (mg/kg)	P (mg/kg)	K (mg/kg)	Salt (mg/kg)	TFS (%)
10/09/2023	934.00 *ton*	Dry-weight		65.3	11,100.00	2,100.00	12,500.00		5.80

	Yield (tons/acre)	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Salt (lbs/acre)
Anticipated harvest content	30.00	240.00	45.00	198.00	0.00
Total actual harvest content	22.78	175.49	33.20	197.62	916.96

2/3

2/3

Field name: 2/3

09/30/2022: Oats, silage-soft dough

Crop: Oats, silage-soft dough Acres planted: 29 Plant date: 09/30/2022

Harvest date	Yield	Reporting basis	Density (lbs/cu ft)	Moisture (%)	N (mg/kg)	P (mg/kg)	K (mg/kg)	Salt (mg/kg)	TFS (%)
05/01/2023	551.00 *ton*	Dry-weight		70.0	17,600.00	4,000.00	32,300.00		9.50

	Yield (tons/acre)	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Salt (lbs/acre)
Anticipated harvest content	16.00	160.00	25.60	132.80	0.00
Total actual harvest content	19.00	200.64	45.60	368.22	1,083.00

05/15/2023: Corn, silage

Crop: Corn, silage Acres planted: 29 Plant date: 05/15/2023

Harvest date	Yield	Reporting basis	Density (lbs/cu ft)	Moisture (%)	N (mg/kg)	P (mg/kg)	K (mg/kg)	Salt (mg/kg)	TFS (%)
10/09/2023	661.00 *ton*	Dry-weight		64.0	11,800.00	2,400.00	11,400.00		5.20

	Yield (tons/acre)	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Salt (lbs/acre)
Anticipated harvest content	30.00	240.00	45.00	198.00	0.00
Total actual harvest content	22.79	193.65	39.39	187.09	853.37

NUTRIENT BUDGET

A. LAND APPLICATIONS

1 - 09/30/2022: Oats, silage-soft dough

Field name: 1

Crop: Oats, silage-soft dough Plant date: 09/30/2022

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
10/26/2022	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	109.60	10.24	103.75	609.94	716,914.00 *gal*
Canal	Surface water	1.03	0.00	0.00	295.27	7,253,603.00 *gal*
Application event totals		110.63	10.24	103.75	905.21	

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
03/18/2023	Pipeline	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	97.24	12.20	154.67	853.62	716,914.00 *gal*
Application event totals		97.24	12.20	154.67	853.62	

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
04/17/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	97.24	12.20	154.67	853.62	716,914.00 *gal*
Canal	Surface water	0.75	0.00	0.00	212.91	5,230,229.00 *gal*
Application event totals		97.99	12.20	154.67	1,066.53	

1 - 05/15/2023: Corn, silage

Field name: 1

Crop: Corn, silage Plant date: 05/15/2023

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following

1 - 05/15/2023: Corn, silage

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
05/10/2023	Towed tank	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Slurry	Process wastewater sludge	152.42	23.39	253.21	1,266.06	1,054,286.00 *gal*
Application event totals		152.42	23.39	253.21	1,266.06	

06/08/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Canal	Surface water	2.31	0.00	0.00	661.26	16,244,253.00 *gal*
Application event totals		2.31	0.00	0.00	661.26	

07/26/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	37.47	6.03	73.65	167.38	253,029.00 *gal*
Canal	Surface water	2.38	0.00	0.00	679.13	16,683,287.00 *gal*
Application event totals		39.85	6.03	73.65	846.51	

08/09/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Canal	Surface water	1.58	0.00	0.00	450.68	11,071,289.00 *gal*
Application event totals		1.58	0.00	0.00	450.68	

08/23/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	37.47	6.03	73.65	167.38	253,029.00 *gal*
Canal	Surface water	1.72	0.00	0.00	491.87	12,082,975.00 *gal*
Application event totals		39.19	6.03	73.65	659.24	

09/08/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Canal	Surface water	2.10	0.00	0.00	601.43	14,774,444.00 *gal*
Application event totals		2.10	0.00	0.00	601.43	

2/3 - 09/30/2022: Oats, silage-soft dough

Field name: 2/3

Crop: Oats, silage-soft dough

Plant date: 09/30/2022

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
10/26/2022	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	96.71	9.04	91.54	538.18	447,429.00 *gal*
Canal	Surface water	1.03	0.00	0.00	295.27	5,130,597.00 *gal*
Application event totals		97.74	9.04	91.54	833.46	

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
03/18/2023	Pipeline	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	80.77	10.13	128.47	709.00	421,174.00 *gal*
Application event totals		80.77	10.13	128.47	709.00	

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
04/17/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	85.80	10.76	136.48	753.20	447,429.00 *gal*
Canal	Surface water	0.75	0.00	0.00	212.91	3,699,431.00 *gal*
Application event totals		86.55	10.76	136.48	966.11	

2/3 - 05/15/2023: Corn, silage

Field name: 2/3

Crop: Corn, silage

Plant date: 05/15/2023

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
05/10/2023	Towed tank	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Slurry	Process wastewater sludge	152.42	23.39	253.21	1,266.06	745,714.00 *gal*
Application event totals		152.42	23.39	253.21	1,266.06	

2/3 - 05/15/2023: Corn, silage

Application date	Application method	Precipitation 24 hours prior	Precipitation during application	Precipitation 24 hours following
06/08/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Canal	Surface water	2.31	0.00	0.00	661.26	11,489,837.00 *gal*
Application event totals		2.31	0.00	0.00	661.26	

07/26/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	49.96	8.03	98.19	223.17	238,629.00 *gal*
Canal	Surface water	2.38	0.00	0.00	679.13	11,800,373.00 *gal*
Application event totals		52.34	8.03	98.19	902.30	

08/09/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Canal	Surface water	1.58	0.00	0.00	450.68	7,830,911.00 *gal*
Application event totals		1.58	0.00	0.00	450.68	

08/23/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Lagoon Water	Process wastewater	49.96	8.03	98.19	223.17	238,629.00 *gal*
Canal	Surface water	1.72	0.00	0.00	491.87	8,546,495.00 *gal*
Application event totals		51.68	8.03	98.19	715.04	

09/08/2023	Surface (irrigation)	No precipitation	No precipitation	No precipitation

Source description	Material type	N (lbs/acre)	P (lbs/acre)	K (lbs/acre)	Salt (lbs/acre)	Amount
Canal	Surface water	2.10	0.00	0.00	601.43	10,450,216.00 *gal*
Application event totals		2.10	0.00	0.00	601.43	

B. NUTRIENT BUDGET

1 - 09/30/2022: Oats, silage-soft dough

Field name: 1 Crop: Oats, silage-soft dough Plant date: 09/30/2022

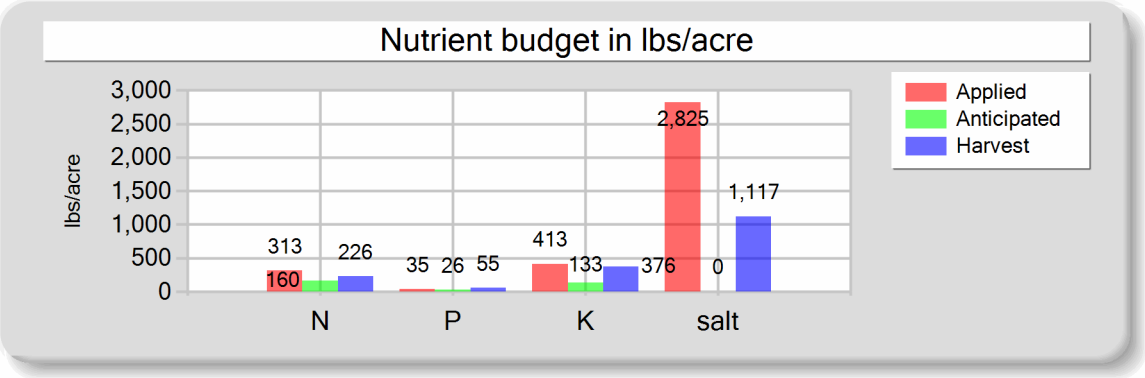

	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Total salt (lbs/acre)
Existing soil nutrient content	0.00	0.00	0.00	0.00
Plowdown credit	0.00	0.00	0.00	0.00
Commercial fertilizer / Other	0.00	0.00	0.00	0.00
Dry manure	0.00	0.00	0.00	0.00
Process wastewater	304.08	34.64	413.09	2,317.18
Fresh water	1.78	0.00	0.00	508.18
Atmospheric deposition	7.00	0.00	0.00	0.00
Total nutrients applied	312.86	34.64	413.09	2,825.36
Anticipated crop nutrient removal	160.00	25.60	132.80	0.00
Actual crop nutrient removal	225.72	54.72	376.20	1,117.20
Nutrient balance	87.14	-20.08	36.89	1,708.16
Applied to removed ratio	1.39	0.63	1.10	2.53

Fresh water applied	
12,483,832.00	*gallons*
459.74	*acre-inches*
11.21	*inches/acre*

Process wastewater applied	
2,150,742.00	*gallons*
79.20	*acre-inches*
1.93	*inches/acre*

Total harvests for the crop	
1	*harvests*

1 - 05/15/2023: Corn, silage

Field name: 1 Crop: Corn, silage Plant date: 05/15/2023

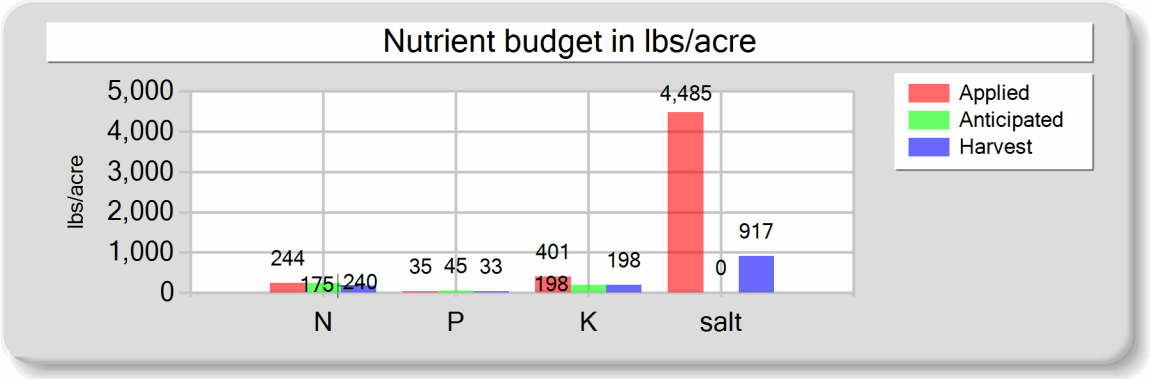

	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Total salt (lbs/acre)
Existing soil nutrient content	0.00	0.00	0.00	0.00
Plowdown credit	0.00	0.00	0.00	0.00
Commercial fertilizer / Other	0.00	0.00	0.00	0.00
Dry manure	0.00	0.00	0.00	0.00
Process wastewater	227.36	35.44	400.50	1,600.81
Fresh water	10.10	0.00	0.00	2,884.37
Atmospheric deposition	7.00	0.00	0.00	0.00
Total nutrients applied	244.46	35.44	400.50	4,485.18
Anticipated crop nutrient removal	240.00	45.00	198.00	0.00
Actual crop nutrient removal	175.49	33.20	197.62	916.96
Nutrient balance	68.97	2.24	202.88	3,568.22
Applied to removed ratio	1.39	1.07	2.03	4.89

Fresh water applied	
70,856,248.00	*gallons*
2,609.39	*acre-inches*
63.64	*inches/acre*

Process wastewater applied	
1,560,344.00	*gallons*
57.46	*acre-inches*
1.40	*inches/acre*

Total harvests for the crop	
1	*harvests*

2/3 - 09/30/2022: Oats, silage-soft dough

Field name: 2/3 Crop: Oats, silage-soft dough Plant date: 09/30/2022

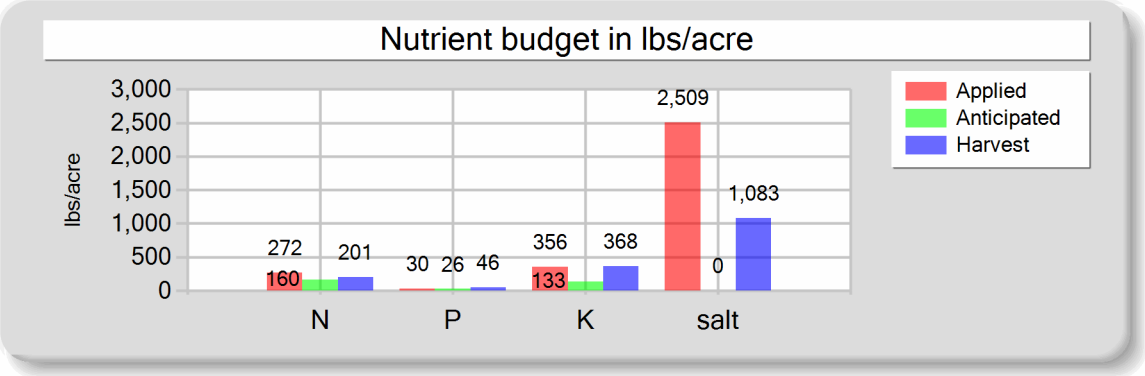

	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Total salt (lbs/acre)
Existing soil nutrient content	0.00	0.00	0.00	0.00
Plowdown credit	0.00	0.00	0.00	0.00
Commercial fertilizer / Other	0.00	0.00	0.00	0.00
Dry manure	0.00	0.00	0.00	0.00
Process wastewater	263.27	29.93	356.49	2,000.38
Fresh water	1.78	0.00	0.00	508.18
Atmospheric deposition	7.00	0.00	0.00	0.00
Total nutrients applied	272.05	29.93	356.49	2,508.56
Anticipated crop nutrient removal	160.00	25.60	132.80	0.00
Actual crop nutrient removal	200.64	45.60	368.22	1,083.00
Nutrient balance	71.41	-15.67	-11.73	1,425.56
Applied to removed ratio	1.36	0.66	0.97	2.32

Fresh water applied	
8,830,028.00	*gallons*
325.18	*acre-inches*
11.21	*inches/acre*

Process wastewater applied	
1,316,032.00	*gallons*
48.46	*acre-inches*
1.67	*inches/acre*

Total harvests for the crop	
1	*harvests*

2/3 - 05/15/2023: Corn, silage

Field name: 2/3 Crop: Corn, silage Plant date: 05/15/2023

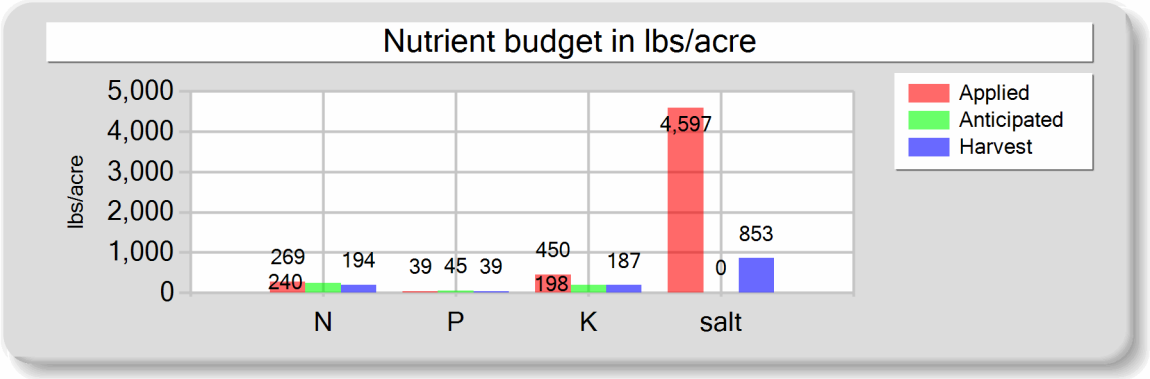

	Total N (lbs/acre)	Total P (lbs/acre)	Total K (lbs/acre)	Total salt (lbs/acre)
Existing soil nutrient content	0.00	0.00	0.00	0.00
Plowdown credit	0.00	0.00	0.00	0.00
Commercial fertilizer / Other	0.00	0.00	0.00	0.00
Dry manure	0.00	0.00	0.00	0.00
Process wastewater	252.35	39.46	449.60	1,712.39
Fresh water	10.10	0.00	0.00	2,884.37
Atmospheric deposition	7.00	0.00	0.00	0.00
Total nutrients applied	269.44	39.46	449.60	4,596.76
Anticipated crop nutrient removal	240.00	45.00	198.00	0.00
Actual crop nutrient removal	193.65	39.39	187.09	853.37
Nutrient balance	75.79	0.07	262.51	3,743.39
Applied to removed ratio	1.39	1.00	2.40	5.39

Fresh water applied	
50,117,832.00	*gallons*
1,845.67	*acre-inches*
63.64	*inches/acre*

Process wastewater applied	
1,222,972.00	*gallons*
45.04	*acre-inches*
1.55	*inches/acre*

Total harvests for the crop	
1	*harvests*

NUTRIENT ANALYSES

A. MANURE ANALYSES

Corral Manure

Sample and source description: Corral Manure

Sample date: 05/10/2023 Material type: Corral solids Source of analysis: Lab analysis Method of reporting: Dry-weight

Moisture: 73.5 %

	Total N (mg/kg)	Total P (mg/kg)	Total K (mg/kg)	Calcium (mg/kg)	Magnesium (mg/kg)	Sodium (mg/kg)	Sulfur (mg/kg)	Chloride (mg/kg)	Total salt (mg/kg)	TFS (%)
Value	21,200.00	4,800.00	28,900.00							0.00
DL	0.01	0.01	0.01							1.00

SSB Manure

Sample and source description: SSB Manure

Sample date: 10/18/2023 Material type: Separator solids Source of analysis: Lab analysis Method of reporting: Dry-weight

Moisture: 65.1 %

	Total N (mg/kg)	Total P (mg/kg)	Total K (mg/kg)	Calcium (mg/kg)	Magnesium (mg/kg)	Sodium (mg/kg)	Sulfur (mg/kg)	Chloride (mg/kg)	Total salt (mg/kg)	TFS (%)
Value	28,200.00	10,000.00	35,900.00							0.00
DL	0.01	0.01	0.01							1.00

B. PROCESS WASTEWATER ANALYSES

2022 Lagoon Q4

Sample and source description: 2022 Lagoon Q4

Sample date: 12/01/2022 Material type: Process wastewater Source of analysis: Lab analysis pH: 7.50

	Kjeldahl-N (mg/L)	NH4-N (mg/L)	NH3-N (mg/L)	Nitrate-N (mg/L)	Total P (mg/L)	Total K (mg/L)	Calcium (mg/L)	Magnes. (mg/L)	Sodium (mg/L)	Bicarb. (mg/L)	Carb. (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	750.00	302.00	0.00	1.10	70.20	711.00								8,180.00	4,180
DL	0.01	0.01	0.01	0.01	0.01	0.01								10.00	1

Lagoon Q1

Sample and source description: Lagoon Q1

Sample date: 03/27/2023 Material type: Process wastewater Source of analysis: Lab analysis pH: 7.50

	Kjeldahl-N (mg/L)	NH4-N (mg/L)	NH3-N (mg/L)	Nitrate-N (mg/L)	Total P (mg/L)	Total K (mg/L)	Calcium (mg/L)	Magnes. (mg/L)	Sodium (mg/L)	Bicarb. (mg/L)	Carb. (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	665.00	489.00	0.00	1.40	83.60	1,060.00								11,400.00	5,850
DL	0.01	0.01	0.01	0.01	0.01	0.01								10.00	1

Slurry

Sample and source description: Slurry

Sample date: 05/10/2023 Material type: Process wastewater sludge Source of analysis: Lab analysis pH: 7.70

	Kjeldahl-N (mg/L)	NH4-N (mg/L)	NH3-N (mg/L)	Nitrate-N (mg/L)	Total P (mg/L)	Total K (mg/L)	Calcium (mg/L)	Magnes. (mg/L)	Sodium (mg/L)	Bicarb. (mg/L)	Carb. (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	705.00	495.00	0.00	5.30	109.00	1,180.00								11,700.00	5,900
DL	0.01	0.01	0.01	0.01	0.01	0.01								10.00	1

Lagoon Q3

Sample and source description: Lagoon Q3

Sample date: 07/26/2023 Material type: Process wastewater Source of analysis: Lab analysis pH: 7.50

	Kjeldahl-N (mg/L)	NH4-N (mg/L)	NH3-N (mg/L)	Nitrate-N (mg/L)	Total P (mg/L)	Total K (mg/L)	Calcium (mg/L)	Magnes. (mg/L)	Sodium (mg/L)	Bicarb. (mg/L)	Carb. (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	727.00	488.00	0.00	0.60	117.00	1,430.00								12,800.00	3,250
DL	0.01	0.01	0.01	0.01	0.01	0.01								10.00	1

Lagoon Q4

Sample and source description: Lagoon Q4

Sample date: 11/06/2023 Material type: Process wastewater Source of analysis: Lab analysis pH: 8.20

	Kjeldahl-N (mg/L)	NH4-N (mg/L)	NH3-N (mg/L)	Nitrate-N (mg/L)	Total P (mg/L)	Total K (mg/L)	Calcium (mg/L)	Magnes. (mg/L)	Sodium (mg/L)	Bicarb. (mg/L)	Carb. (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	280.00	214.00	0.00	0.00	58.90	584.00								6,110.00	3,300
DL	0.01	0.01	0.01	0.01	0.01	0.01								10.00	1

C. FRESH WATER ANALYSES

Canal

CCID Canal

Sample description: CCID Canal

Sample date: 10/17/2023 Source of analysis: Lab analysis

	Total N (mg/L)	NH4-N (mg/L)	Nitrate-N (mg/L)	Calcium (mg/L)	Magnesium (mg/L)	Sodium (mg/L)	Bicarbonate (mg/L)	Carbonate (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	0.70	0.00	0.70								328.00	200
DL	0.01	0.01	0.01								10.00	1

Domestic Well

DW-MB

Sample description: DW-MB

Sample date: 12/11/2023 Source of analysis: Lab analysis

	Total N (mg/L)	NH4-N (mg/L)	Nitrate-N (mg/L)	Calcium (mg/L)	Magnesium (mg/L)	Sodium (mg/L)	Bicarbonate (mg/L)	Carbonate (mg/L)	Sulfate (mg/L)	Chloride (mg/L)	EC (µmhos/cm)	TDS (mg/L)
Value	13.50	0.00	13.50								1,780.00	0
DL	0.01	0.01	0.01								10.00	1

D. SOIL ANALYSES

No soil analyses entered.

E. PLANT TISSUE ANALYSES

1 - 09/30/2022: Oats, silage-soft dough

1 - 09/30/2022: Oats, silage-soft dough

Field 1 Oats

Sample and source description: Field 1 Oats

Sample date: 05/01/2023 Source of analysis: Lab analysis Method of reporting: Dry-weight

Moisture: 55.3 %

	Total N (mg/kg)	Total P (mg/kg)	Total K (mg/kg)	Total salt (mg/kg)	TFS (%)
Value	19,800.00	4,800.00	33,000.00		9.80
DL	0.01	0.01	0.01		1.00

1 - 05/15/2023: Corn, silage

Field 1 Corn

Sample and source description: Field 1 Corn

Sample date: 10/09/2023 Source of analysis: Lab analysis Method of reporting: Dry-weight

Moisture: 65.3 %

	Total N (mg/kg)	Total P (mg/kg)	Total K (mg/kg)	Total salt (mg/kg)	TFS (%)
Value	11,100.00	2,100.00	12,500.00		5.80
DL	0.01	0.01	0.01		1.00

2/3 - 09/30/2022: Oats, silage-soft dough

Field 2/3-Oats

Sample and source description: Field 2/3-Oats

Sample date: 05/01/2023 Source of analysis: Lab analysis Method of reporting: Dry-weight

Moisture: 54.7 %

	Total N (mg/kg)	Total P (mg/kg)	Total K (mg/kg)	Total salt (mg/kg)	TFS (%)
Value	17,600.00	4,000.00	32,300.00		9.50
DL	0.01	0.01	0.01		1.00

2/3 - 05/15/2023: Corn, silage

Fields 2/3 Corn

Sample and source description: Fields 2/3 Corn

Sample date: 10/09/2023 Source of analysis: Lab analysis Method of reporting: Dry-weight

Moisture: 64.0 %

	Total N (mg/kg)	Total P (mg/kg)	Total K (mg/kg)	Total salt (mg/kg)	TFS (%)
Value	11,800.00	2,400.00	11,400.00		5.20
DL	0.01	0.01	0.01		1.00

F. SUBSURFACE (TILE) DRAINAGE ANALYSES

No subsurface (tile) drainage analyses entered.

NUTRIENT APPLICATIONS, POTENTIAL REMOVAL, AND BALANCE

A. SUMMARY OF NUTRIENT APPLICATIONS, POTENTIAL REMOVAL, AND BALANCE

	Total N (lbs)	Total P (lbs)	Total K (lbs)	Total salt (lbs)
Existing soil nutrient content	0.00	0.00	0.00	0.00
Plowdown credit	0.00	0.00	0.00	0.00
Commercial fertilizer / Other	0.00	0.00	0.00	0.00
Dry manure	0.00	0.00	0.00	0.00
Process wastewater	36,742.02	4,885.73	56,734.04	268,308.04
Fresh water	831.18	0.00	0.00	237,478.57
Atmospheric deposition	980.00	0.00	0.00	0.00
Total nutrients applied	38,553.20	4,885.73	56,734.04	505,786.61
Anticipated crop nutrient removal	28,000.00	4,942.00	23,156.00	0.00
Actual crop nutrient removal	27,883.91	6,069.34	39,630.52	139,555.41
Nutrient balance	10,669.29	-1,183.61	17,103.52	366,231.20
Applied to removed ratio	1.38	0.80	1.43	3.62

B. POUNDS OF NUTRIENT APPLIED VS. CROP REMOVAL

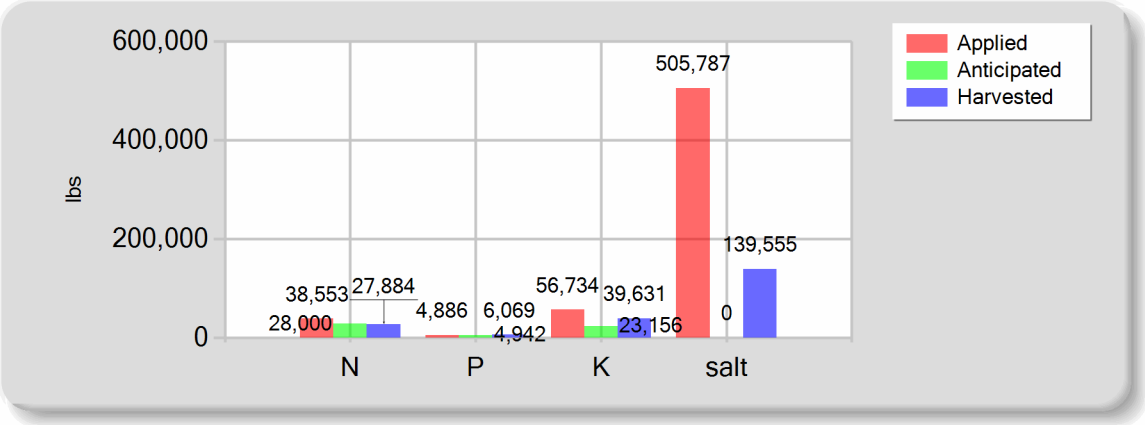

C. POUNDS OF NUTRIENT APPLIED BY MATERIAL TYPE

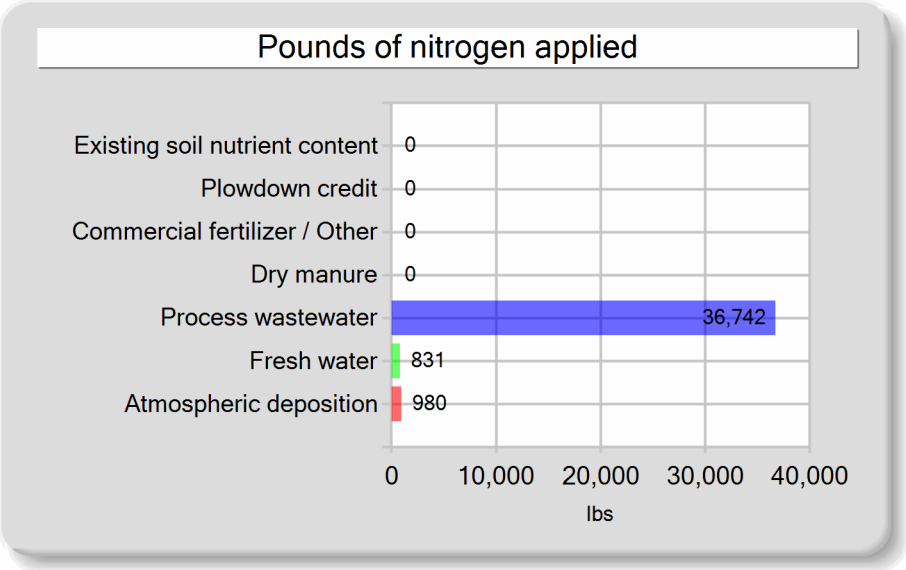

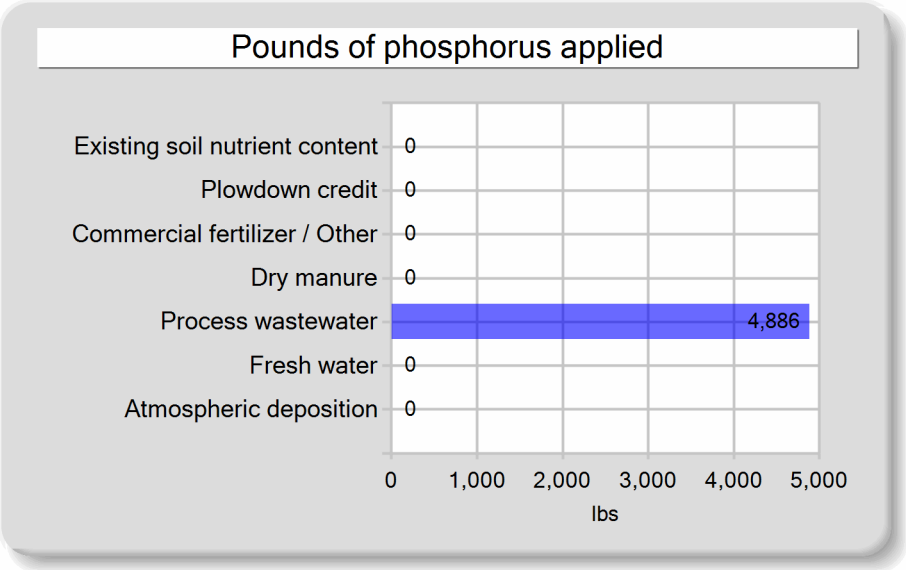

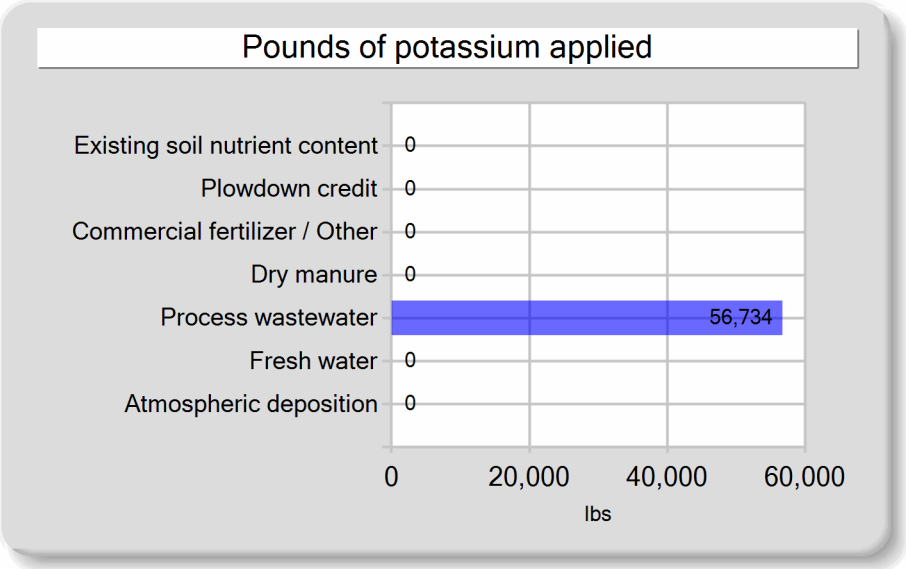

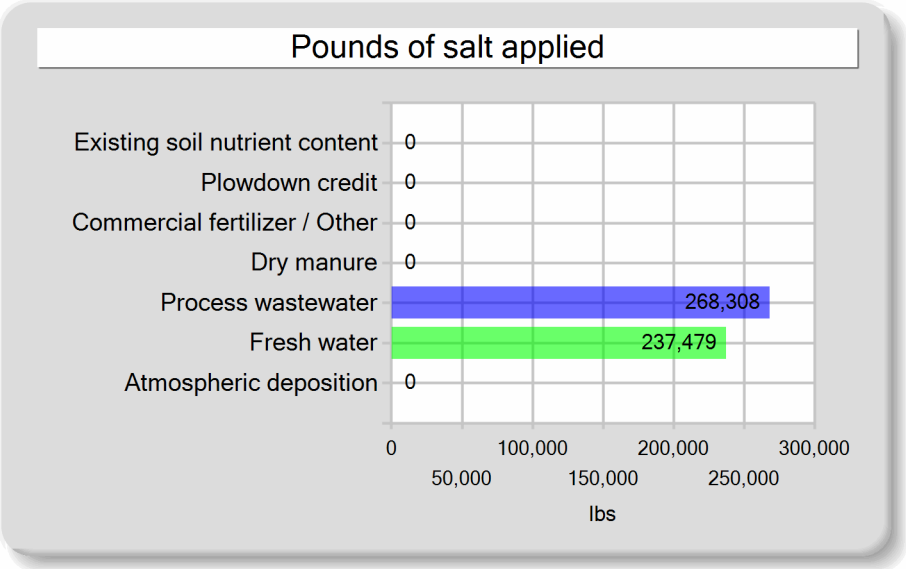

EXCEPTION REPORTING

A. MANURE, PROCESS WASTEWATER, AND OTHER DAIRY WASTE DISCHARGES

The following is a summary of all manure and process wastewater discharges from the production area to surface water or to land areas (land application areas or otherwise) when not in accordance with the facility's Nutrient Management Plan.

No manure or process wastewater discharges occurred during the reporting period.

B. STORM WATER DISCHARGES

The following is a summary of all storm water discharges from the production area to surface water during the reporting period when not in accordance with the facility 's Nutrient Management Plan.

No stormwater discharges occurred during the reporting period.

C. LAND APPLICATION AREA TO SURFACE WATER DISCHARGES

The following is a summary of all discharges from the land application area to surface water that have occurred during the reporting period when not in accordance with the facility's Nutrient Management Plan.

No land application area to surface water discharges occurred during the reporting period.

NUTRIENT MANAGEMENT PLAN AND EXPORT AGREEMENT STATEMENTS

A. NUTRIENT MANAGEMENT PLAN STATEMENTS

Was the facility's NMP updated in the reporting period?	Yes
Was the facility's NMP developed by a certified nutrient management planner (specialist) as specified in Attachment C of the General Order?	Yes
Was the facility's NMP approved by a certified nutrient management planner (specialist) as specified in Attachment C of the General Order?	Yes

B. EXPORT AGREEMENT STATEMENT

Are there any written agreements with third parties to receive manure or process wastewater that are new or were revised within the reporting period?	No

ADDITIONAL NOTES

A. NOTES

No notes entered for this annual report.

CERTIFICATION

A. OWNER AND/OR OPERATOR CERTIFICATION

I certify under penalty of law that I have personally examined and am familiar with the information submitted in this document and all attachments and that, based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment.

Joe Barcellos	Michael Barcellos
SIGNATURE OF OWNER OF FACILITY	SIGNATURE OF OPERATOR OF FACILITY
Joe Barcellos	Mike Barcellos
PRINT OR TYPE NAME	PRINT OR TYPE NAME
Jun 28, 2024	Jun 28, 2024
DATE	DATE

ATTACHMENTS

A. REQUIRED ATTACHMENTS

The following lists the required documents that should be attached to the Annual Report when submitted .

Annual Dairy Facility Assessment
Provide an Annual Dairy Facility Assessment (an update to the Preliminary Dairy Facility Assessment in Attachment A) for each reporting period. On the PDFA Final page, click on the ADFA Report button to generate an ADFA report after updating information as needed .

Manure/Process Wastewater Tracking Manifests
Provide copies of all manure/process wastewater tracking manifests for the reporting period, signed by both the owner/operator and the hauler.

Corrective Actions Documents
Provide records documenting any corrective actions taken to correct deficiencies noted as a result of the inspections required in the Monitoring Requirements of the General Order. Deficiencies not corrected in 30 days must be accompanied by an explanation of the factors preventing immediate correction.

Groundwater Monitoring
Dischargers that monitor supply wells or subsurface (tile) drainage systems, or that have monitoring well systems must submit monitoring results as directed in the General Order, Groundwater Reporting Section starting on page MRP-13.

Storm Water Monitoring
Dischargers that are required to monitor storm water more frequently than required in the General Order must submit monitoring results as directed in the General Order, Storm Water Reporting Section on page MRP-14.

ATTACHMENT D

Manure/Process Wastewater Tracking Manifest
For
Existing Milk Cow Dairies

Instructions:

1) Complete one manifest for each hauling event, for each destination. A hauling event may last for several days, as long as the manure is being hauled to the same destination.
2) If there are multiple destinations, **complete a separate form for each destination**.
3) The operator must obtain the signature of the hauler upon completion of each manure-hauling event.
4) The operator shall submit copies of manure/process wastewater tracking manifest(s) with the Annual Monitoring Report for Existing Milk Cow Dairies.

Operator Information:

Name of Operator: MIKE BARCELLOS

Name of Dairy Facility: MONSTER DAIRY

Facility Address: 1048 LUNDY RD (Number and Street) NEWMAN CA (City) 95360 (Zip Code)

Contact Person Name and Phone Number: MIKE BARCELLOS (Name) 209-678-1792 (Phone Number)

Manure/Process Wastewater Hauler Information:

Name of Hauling Company/Person: ALP CUSTOM SPREADING

Address of Hauling Company /Person: PO BOX 218 (Number and Street) NEWMAN CA (City) 95360 (Zip Code)

Contact Person: JEFF LIMA (Name) 209-862-3393 (Phone Number)

Destination Information:

Composting Facility / Broker / Farmer / Other (identify) AJ BORBA HOLSTEINS (please circle one)

Contact information of Composting Facility, Broker, Farmer, or Other (as identified above):

Name	Number and Street	City	Zip Code	Phone Number
TONY BORBA	PO BOX 670	HILMAR CA	95324	

Manure/Process Wastewater Destination Address or Assessor's Parcel Number:

Number and Street	City	Zip Code	Assessor's Parcel Number
RIVER RD	NEWMAN CA	95360	

Dates Hauled: 5/22/23

Amount Hauled:

Enter the amount of manure hauled in tons or cubic yards (indicate the units used), the manure solids content (if amount reported in tons) or manure density (if amount reported in cubic yards), and the method used to calculate the amount:

Manure: 3,666 Tons or Cubic Yards (indicate which units used)
Manure Solids Content (if amount reported in tons): _____
Manure Density (if amount reported in cubic yards): _____

Method used to determine amount of manure: TONS PER LOAD

_____

Enter the amount of process wastewater hauled in gallons and the method used to determine the amount.

Process Wastewater: _____ Gallons

Method used to determine volume of process wastewater: _____

_____

Written Agreement:
Does the Operator have a written agreement (in compliance with Land Application Specification C.2 of Waste Discharge Requirements General Order No. R5-2007-0035) with any party that receives process wastewater from the Operator for its own use? (please check one)

____ Yes _____ No

If the answer is no, the Operator agrees to have such a written agreement with any such party for any process wastewater transferred after **31 December 2007** to such party.
_____ (Operator shall provide initials here to acknowledge this requirement).

Certification:
I declare under the penalty of law that I personally examined and am familiar with the information submitted in this document, and that based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of a fine and imprisonment for knowing violations.

Operator's Signature: Michael Barcellos Date: 5/22/23

Hauler's Signature: jeff lima Date: 5/22/23

Report of Dairy Well Water Analysis

DELLAVALLE LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman CA 95360
00-0021391 08

E-mail:
Copy To: cas.labs@yahoo.com

Lab No.: 23L0708
Sampled By: M Dekeyrel
Requested By: Mike Barcellos
Submitted Date: 12/12/23
Reported Date: 12/18/23
Project:
Crop ID:

		Date Sampled	Time Sampled	EC µmhos/cm	EC mmhos/cm	NO_3-N mg/L	Field NH_4-N mg/L	Total NH_4-N mg/L	pH at 25°C unit
1	DW - MB	12/11/23	16:55	1780	1.78	13.5	ND		7.7

***** = Field NH_4-N not Taken.
ND = None Detected

Approved By: Scott M Friedland
Laboratory Director\Technical Manager
ELAP Certification #1595
A2LA Certification #6440.02

DELLAVALLE LABORATORY INC

Report of Dairy Well Water Analysis

Monster Dairy
1048 Lundy Road
Newman CA 95360
00-0021391 08

E-mail:
Copy To: cas.labs@yahoo.com

Lab No.: 23L0708
Sampled By: M Dekeyrel
Requested By: Mike Barcellos
Submitted Date: 12/12/23
Reported Date: 12/18/23
Project:
Crop ID:

		Date Sampled	Time Sampled	EC µmhos/cm	EC mmhos/cm	NO_3-N mg/L	Nitrogen agricultural use Calcs calculated from nitrate-N lbs/AcFoot	lbs/AcInch
1	DW - MB	12/11/23	16:55	**1780**	**1.78**	**13.5**	36.86	3.07

Water for Crop Use **Nutrient Management**	Total Salts	Total Salts	Nitrate Nitrogen
Low Levels	< 900	< 0.90	< 2.0
Significant Levels	900-2200	0.90-2.2	2.0-10.0
High Levels	2200+	2.2+	10.0+

Sampling abbreviations: H.B. = hose bib, S.P. = stand pipe, Dom. = domestic well, IR = irrigation well, AG = ag well.
Nitrate exceeds Water Quality MCL levels if results are above 10 mg/l nitrate-nitrogen NO3-N (equivalent to 45 mg/l nitrate, NO3).
Total Salt results are used to monitor changes of salt in the well aquifers between annual tests.
MCL = Maximum Contaminant Level according to the California Domestic Water Quality and Monitoring Regulations (Title 22)
MDL = Method Detection Limit; **RL** = Reporting Limit, mg/L = ppm.
SM = Standard Methods for the Examination of Water and Wastewater
EPA = Environmental Protection Agency methods used unless otherwise indicated.

DELLAVALLE™
LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman, CA 95360

Account# 00-0021391
Account Manager: Ben Nydam
Submitted By: Mike Barcellos

Received: 12/12/2023 15:53
Reported: 12/18/2023 13:41

Samples in this Report

Lab ID	Sample	Matrix	Sampled By	Crop	Date Sampled
23L0708-01	DW - MB	Well Water	M Dekeyrel		12/11/2023 16:55

Default Cooler Temperature on Receipt °C: -2.4
Containers Intact
COC/Labels Agree
Received On Ice

Notes and Definitions

Item	Definition
H	Hold Time Exceeded
MCL	Drinking Water Maximum Contaminant Level
ND	Analyte NOT DETECTED at or above the reporting limit.
NES	Not Enough Sample
*	Not Taken
RPD	Relative Percent Difference
%REC	Percent Recovery
Source	Sample that was matrix spiked or duplicated.

Scott McFriedland

Laboratory Director/Technical Manager

ELAP Certification #1595
A2LA Certification #6440.02

The results in this report apply to the samples as received and were analyzed in accordance with the chain of custody document. This analytical report must be reproduced in its entirety. All results listed in this report are for the exclusive use of the submitting party. Dellavalle Laboratory, Inc. assumes no responsibility for report alteration, separation, detachment or third party interpretation.

DELLAVALLE™
LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman, CA 95360

Account# 00-0021391
Account Manager: Ben Nydam
Submitted By: Mike Barcellos

Received: 12/12/2023 15:53
Reported: 12/18/2023 13:41

Sample Results

Sample: DW - MB
23L0708-01 (Water)

Sampled: 12/11/2023 16:55
Sampled By: M Dekeyrel

Analyte	Result	Units	Reporting Limit	DIL	DW MCL	Date/Time Analyzed	Method	Notes	Batch
Electrical Conductivity	**1.78**	mmhos/cm	0.01	1		12/13/23 17:47	SM 2510 B		BEL0498
Electrical Conductivity umhos	**1780**	umhos/cm	10.0	1		12/13/23 17:47	SM 2510 B		BEL0498
Ammonia (as N)	ND	mg/L	0.00	1		12/11/23 16:55	Field		BEL0391
Nitrate Nitrogen as NO3N	**13.5**	mg/L	0.1	1	10	12/13/23 15:23	EPA 300.0		BEL0444
Temperature	**25.0**	units	0.0	1		12/13/23 17:47	SM 4500-H+	H	BEL0498
pH	**7.7**	units	1.0	1		12/13/23 17:47	SM 4500-H+	H	BEL0498

The results in this report apply to the samples as received and were analyzed in accordance with the chain of custody document. This analytical report must be reproduced in its entirety. All results listed in this report are for the exclusive use of the submitting party. Dellavalle Laboratory, Inc. assumes no responsibility for report alteration, separation, detachment or third party interpretation.

DELLAVALLE™ LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman, CA 95360

Account# 00-0021391
Account Manager: Ben Nydam
Submitted By: Mike Barcellos

Received: 12/12/2023 15:53
Reported: 12/18/2023 13:41

Quality Control

Analyte	Result	Qual	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit
Batch: BEL0444										
Blank (BEL0444-BLK1)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	ND		0.1	mg/L						
Blank (BEL0444-BLK2)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	ND		0.1	mg/L						
Blank (BEL0444-BLK3)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	ND		0.1	mg/L						
Blank (BEL0444-BLK4)					Prepared: 12/13/2023 Analyzed: 12/14/2023					
Nitrate Nitrogen as NO3N	ND		0.1	mg/L						
LCS (BEL0444-BS1)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	5.2		0.1	mg/L	5.000		103	90-110		
LCS (BEL0444-BS2)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	5.2		0.1	mg/L	5.000		104	90-110		
LCS (BEL0444-BS3)					Prepared: 12/13/2023 Analyzed: 12/14/2023					
Nitrate Nitrogen as NO3N	5.2		0.1	mg/L	5.000		103	90-110		
Duplicate (BEL0444-DUP1)		**Source: 23L0740-02**			Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	0.05		0.1	mg/L		0.05			3.92	10
Duplicate (BEL0444-DUP2)		**Source: 23L0744-02**			Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	0.05		0.1	mg/L		0.05			1.98	10
Duplicate (BEL0444-DUP3)		**Source: 23L0700-01**			Prepared: 12/13/2023 Analyzed: 12/14/2023					
Nitrate Nitrogen as NO3N	0.04		0.1	mg/L		0.04			0.00	10
Matrix Spike (BEL0444-MS1)		**Source: 23L0740-02**			Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	5.1		0.1	mg/L	5.000	0.05	101	90-110		
Matrix Spike (BEL0444-MS2)		**Source: 23L0744-02**			Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	5.1		0.1	mg/L	5.000	0.05	100	90-110		
Matrix Spike (BEL0444-MS3)		**Source: 23L0700-01**			Prepared: 12/13/2023 Analyzed: 12/14/2023					
Nitrate Nitrogen as NO3N	5.1		0.1	mg/L	5.000	0.04	102	90-110		
Reference (BEL0444-SRM1)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	10.1			mg/L	10.00		101	90-110		
Reference (BEL0444-SRM2)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	10.2			mg/L	10.00		102	90-110		

The results in this report apply to the samples as received and were analyzed in accordance with the chain of custody document. This analytical report must be reproduced in its entirety. All results listed in this report are for the exclusive use of the submitting party. Dellavalle Laboratory, Inc. assumes no responsibility for report alteration, separation, detachment or third party interpretation.

DELLAVALLE™
LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman, CA 95360

Account# 00-0021391
Account Manager: Ben Nydam
Submitted By: Mike Barcellos

Received: 12/12/2023 15:53
Reported: 12/18/2023 13:41

Quality Control
(Continued)

Analyte	Result	Qual	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit
Batch: BEL0444 (Continued)										
Reference (BEL0444-SRM3)					Prepared & Analyzed: 12/13/2023					
Nitrate Nitrogen as NO3N	10.2			mg/L	10.00		102	90-110		
Reference (BEL0444-SRM4)					Prepared: 12/13/2023 Analyzed: 12/14/2023					
Nitrate Nitrogen as NO3N	10.2			mg/L	10.00		102	90-110		

The results in this report apply to the samples as received and were analyzed in accordance with the chain of custody document. This analytical report must be reproduced in its entirety. All results listed in this report are for the exclusive use of the submitting party. Dellavalle Laboratory, Inc. assumes no responsibility for report alteration, separation, detachment or third party interpretation.

DELLAVALLE™ LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman, CA 95360

Account# 00-0021391
Account Manager: Ben Nydam
Submitted By: Mike Barcellos

Received: 12/12/2023 15:53
Reported: 12/18/2023 13:41

Quality Control
(Continued)

Analyte	Result	Qual	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit
Batch: BEL0498										
Blank (BEL0498-BLK1)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	ND		0.01	mmhos/cm						
Temperature	25.0		0.0	units						
Electrical Conductivity umhos	ND		10.0	umhos/cm						
pH	5.5		1.0	units						
Blank (BEL0498-BLK2)					Prepared & Analyzed: 12/13/2023					
Temperature	25.0		0.0	units						
Electrical Conductivity	ND		0.01	mmhos/cm						
Electrical Conductivity umhos	ND		10.0	umhos/cm						
pH	7.7		1.0	units						
Blank (BEL0498-BLK3)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	ND		0.01	mmhos/cm						
Temperature	25.0		0.0	units						
Electrical Conductivity umhos	ND		10.0	umhos/cm						
pH	7.7		1.0	units						
Duplicate (BEL0498-DUP1)		**Source: 23L0716-01**			Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	2.02		0.01	mmhos/cm		2.00			0.916	10
pH	7.4		1.0	units		7.4			0.135	10
Electrical Conductivity umhos	2020		10.0	umhos/cm		2000			0.916	10
Duplicate (BEL0498-DUP2)		**Source: 23L0724-02**			Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	2.08		0.01	mmhos/cm		2.04			2.11	10
Electrical Conductivity umhos	2080		10.0	umhos/cm		2040			2.11	10
pH	7.3		1.0	units		7.3			0.274	10
Reference (BEL0498-SRM1)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	436			umhos/cm	426.0		102	90-110		
Reference (BEL0498-SRM2)					Prepared & Analyzed: 12/13/2023					
pH	7.5			units	7.520		100	67021-101.32		
Reference (BEL0498-SRM3)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	1050			umhos/cm	1000		105	90-110		
Electrical Conductivity umhos	1050			umhos/cm	1000		105	90-110		
Reference (BEL0498-SRM4)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	1070			umhos/cm	1000		107	90-110		
Electrical Conductivity umhos	1070			umhos/cm	1000		107	90-110		
Reference (BEL0498-SRM5)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity	1090			umhos/cm	1000		109	90-110		

The results in this report apply to the samples as received and were analyzed in accordance with the chain of custody document. This analytical report must be reproduced in its entirety. All results listed in this report are for the exclusive use of the submitting party. Dellavalle Laboratory, Inc. assumes no responsibility for report alteration, separation, detachment or third party interpretation.

DELLAVALLE™ LABORATORY INC

Monster Dairy
1048 Lundy Road
Newman, CA 95360

Account# 00-0021391
Account Manager: Ben Nydam
Submitted By: Mike Barcellos

Received: 12/12/2023 15:53
Reported: 12/18/2023 13:41

Quality Control
(Continued)

Analyte	Result	Qual	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit
Batch: BEL0498 (Continued)										
Reference (BEL0498-SRM5)					Prepared & Analyzed: 12/13/2023					
Electrical Conductivity umhos	1090			umhos/cm	1000		109	90-110		
Reference (BEL0498-SRM6)					Prepared & Analyzed: 12/13/2023					
pH	4.0			units	4.000		101	97.5-102.5		
Reference (BEL0498-SRM7)					Prepared & Analyzed: 12/13/2023					
pH	4.0			units	4.000		101	97.5-102.5		
Reference (BEL0498-SRM8)					Prepared & Analyzed: 12/13/2023					
pH	4.0			units	4.000		100	97.5-102.5		

The results in this report apply to the samples as received and were analyzed in accordance with the chain of custody document. This analytical report must be reproduced in its entirety. All results listed in this report are for the exclusive use of the submitting party. Dellavalle Laboratory, Inc. assumes no responsibility for report alteration, separation, detachment or third party interpretation.

12/12/23 15:53 23L0708

JG

DELLAVALLE LABORATORY, INC.

1910 W. McKinley Avenue, Suite 110 • Fresno, CA 93728
www.dellavallelab.com 559 233-6129 • 800 228-9896 • Fax 559 268-8174

WATER WORK REQUEST

Bill To: Acct No. 21391 Cons. 8

Purchase Order No. _____ Results Needed By _____

Client: **Monster Dairy**
Address: 1048 Lundy Road
City, State, Zip: Newman, CA 95360
Phone _____ Fax _____
Cell/Email _____

Copy to: Cardoso Ag Sevices - cas.labs@yahoo.com

Requested by: Mike Barcellos - (209) 678-1792

Ranch _____

Date sampled: 12/11/23

Sampled by: MDekeuvel

[X] QA/QC Document [X] Copy of Chain [ ] RWQCB

No. of Samples _____ No. Bottles _____

Water Type: [ ] Drinking [ ] Wastewater
[ ] Ag Water [ ] Ground Water [ ] Mon. Well
[ ] Supply Water [ ] Other _____

Analysis and Bottles Required: *(Please Indicate Analysis)*

(✓) DWW1: (EC, pH, NO_3-N, **NH_4-N Field Test)**
(1) l L plastic, unpreserved (white)

( ) DWW2: (DWW1 Plus SO_4, CO_3, HCO_3, Cl, Ca, Mg, Na, TDS)
(1) l L plastic, unpreserved (white)

( ) DCW1: (EC, NO_3-N, TDS)
(1) l L plastic, unpreserved (white)

( ) DPW1: (EC, pH, NO_3-N, NH_4-N, TKN, TDS, TP, TK)
(1) l L plastic, unpreserved (white)

( ) DPW2: (DPW1 Plus Ca, Mg, Na, HCO_3, CO_3, SO_4, Cl)
(1) l L plastic, unpreserved (white)

( ) Other _____

DESCRIPTION OF SAMPLES

		Date Sampled	Time Sampled	Field NH4-N (mg/L)	Received Temp °C
1. DW-MB	Sampled From:	12/11/23	455p	0	-2.4
2.	Sampled From:				
3.	Sampled From:				
4.	Sampled From:				
5.	Sampled From:				
6.	Sampled From:				
7.	Sampled From:				
8.	Sampled From:				
9.	Sampled From:				
10.	Sampled From:				

IR Thermometer SN: 192603727
Correction Factor: 0°C
Calibration Due: 03/06/2024
Location: Laboratory

CHAIN OF CUSTODY

Carrier	Signature	Company	Received (Date/Time)	Relinquished (Date/Time)
First	MDekeuvel	CASINC	12/11/23 455p	12/12/23 @ 9:30am
Second	JLF	DLV	12-12-23 9:30	12-12-23 2:01
Third	MM	DLI	12/12 15:53	
Fourth				

I guarantee that as the client, or on behalf of the client named, I have the authority to contract the above requested services. Should it be found that I do not have such authority, I agree to be personally liable for all costs and, if there should be action against me for this breach, reasonable attorneys' fees. It is understood that payment is expected to be cash with samples unless terms have been previously arranged. Terms are net 30 days; overdue accounts will be charged a dated damage fee of 2% per month (annually 24 %) or $5.00 per month whichever is greater.

If payment is not made when due and a legitimate dispute exists concerning the product or services of Dellavalle Laboratory, Inc., it will be submitted to mediation under the Rules and Procedures of Creative Alternative to Litigation, Inc. (cal). If the dispute is not resolved in mediation, then the dispute will be submitted to binding arbitration through cal under its Rules and Procedures. The prties will equally bear the costs of mediation/arbitration. If, however, the mediator declares that no legitimate dispute exists, then debtor will pay all mediation and arbitration costs, and in the event of arbitration, reasonable attorneys' fees of Dellavalle Laboratory.

Invoicing Information:

Sampling Hrs ____ Miles ____ Consulting ____

Amt Paid ____ Rec By ____ Check No. ____

Shipping

$ _____ In
$ _____ Out
Date _____

Signature _____

Sample received in cooler with ice?
[ ] Yes [ ] No

ctl:update 2020

Shipping Information: Shipped In ☐ Picked-Up ☒ Walk In ☐ DLI Sampler ☐ Other ☐ _____

Container: Ice Chest ☒ Box ☐ None ☐ | **Refrigerant:** Wet Ice ☒ Blue Ice ☐ None ☐

Samples Preserved with HNO_3 or H_2SO_4 were: ☐ Received Preserved ☐ Preserved Upon Receipt at Laboratory

Type of Container(s) Received		Sample Number 1	2	3	4	5	6	7	8	9	10
Sample Containers for Internal (DLI) Use *(Containers that go into the Lab)*											
Plastics	100 mL sterile plastic $Na_2S_2O_3$ (Green)										
	250 mL unpreserved (White) Plastic										
	250 mL HNO_3 (Red) Plastic										
	* pH Value										
	250 mL H_2SO_4 (Yellow) Plastic										
	* pH Value										
	500 mL unpreserved (White) Plastic										
	1 L unpreserved (White) Plastic										
	1 L unpreserved (BOD) (Purple) Plastic										
"	500mL unpreserved (White) Glass										
	PO4-P Kit										
	Other:										
Sample Containers for Subcontracted ("Send Out") Analyses *(Containers that go in the Subcontract ("Send Out") Refrigerator)*											
Plastics	100 mL sterile plastic $Na_2S_2O_3$ (Green)										
	250 mL unpreserved (White) Plastic										
	250 mL HNO_3 (Red) Plastic										
	250 mL H_2SO_4 (Yellow) Plastic										
	500 mL HNO_3 (Red)										
	1 L unpreserved (White) Plastic										
	1 L unpreserved (BOD) (Purple) Plastic										
	1 L HNO_3 (Red)										
VOA Vials	40 mL AG VOA, $Na_2S_2O_3$ + MCAA										
	40 mL AG VOA, $Na_2S_2O_3$										
	40mL AG VOA unpreserved (White) (Set of 3										
	40 mL AG VOA, $Na_2S_2O_3$ (Green) (Set of 3)										
	40mL VOA, H_3PO_4 (Set of 3)										
	40 mL VOA, HCl (Blue) (Set of 3)										
	40 mL VOA, $Na_2S_2O_3$ (Green) (Set of 3)										
Glass	250 mL AG unpreserved (White)										
	250 mL AG H_2SO_4 (Yellow)										
	250 mL AG $Na_2S_2O_3$ (Green)										
	250 mL AG $Na_2S_2O_3$ + MCAA										
	500 mL glass unpreserved (White)										
	500 mL AG HCl (Blue)										
	1 L AG unpreserved (White)										
	1 L AG H_2SO_4 (Yellow)										
	1 L AG $Na_2S_2O_3$ (Green)										
	1 L AG HCl (Blue)										
Special	Cr^{6+} - 50mL Plastic w/Borate/HCO_3/CO_3										
	Cyanide - 500 mL NaOH										
	Asbestos - 1L P wrapped in foil (Set of 2)										
	Sulfide - 1 L **AG** or **P** NaOH + ZnAc										
	Chlorite/Bromate - 250 mL AG with EDA										
	HAA5 - 250mL AG Ammonium Chlorite										
	DO KIT										
	Other:										
	Other:										

12/12/23 15:53 23L0708

SEND OUT
